


RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

For ease of navigating this document please click on the relevant icon



FLOOD RECOVERY ROAD PROJECTS MAP

The projects listed on this dashboard have been identified as Essential Public Asset Reconstruction Works that are being funded by the Disaster Recovery Funding Arrangements provided by the State and Commonwealth Governments, administered by Hawkesbury City Council and Transport for NSW on their behalf.

Our [roads projects map](#) has been regrouped by project type and can be found on the Hawkesbury City Council website under the Renewing Hawkesbury's Roads banner. Currently, the map is only showing projects identified as Essential Public Asset Reconstruction Works that are being funded by the Disaster Recovery Funding Arrangements provided by State and Commonwealth.



HCC, Central Coast Council and Delaney Civil meet on Wednesday 23 August to discuss the upcoming commencement of the Settlers Road Landslip and Thomas James Bridge.

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

MAJOR PROJECT – SETTLERS ROAD, Thomas James Bridge

Project Manager Sadat Rahman

Thomas James Bridge (1830) – Monitoring and Reconstruction

- Council has engaged Delaney Civil to carry out the remedial works at Thomas James Bridge.
- Early planning has commenced for the relocation of two power poles and the removal of redundant Telstra poles and cables. In addition, on 16 August 2023 we submitted our application with NSW Heritage for a S140 permit to ensure archaeological relics are excavated under appropriate supervision.
- The bridge continues to be monitored autonomously and HCC also have desktop CCTV.
- 24/7 Traffic Control is in place enforcing the 5-tonne load limit.

Community Advisory Group

- As part of our commitment to keeping the community informed, Council held two community meetings, one in-person and one online, on Monday 31 July 2023



Settlers Road Landslip

- HCC working with CCC to achieve funding approval by TfNSW North Region by end of August.
- GHD, CCC and HCC are holding fortnightly progress design meetings. GHD submitted 100% design on 04 August 2023.
- Early clearing is expected to commence from September 2023 pending on approval received from CCC and Transport. Landslip clearing work will reinstate two lanes of traffic on Settlers Road which will help provide better access conditions for residents once the temporary bridge is constructed.

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

VALLEY WAY, Tennyson

Project Manager Rajesh Lama

J&G Excavations commenced embankment restoration and road reconstruction 24 July 2023.

Culvert headwall and gabian wall is now complete.


Sydney Water have commenced repairs to the damaged water main this week.

Traffic control is on site to ensure safe thoroughfare.



GORRICKS RUN CAUSEWAY, Upper Macdonald

Project Manager Rajesh Lama

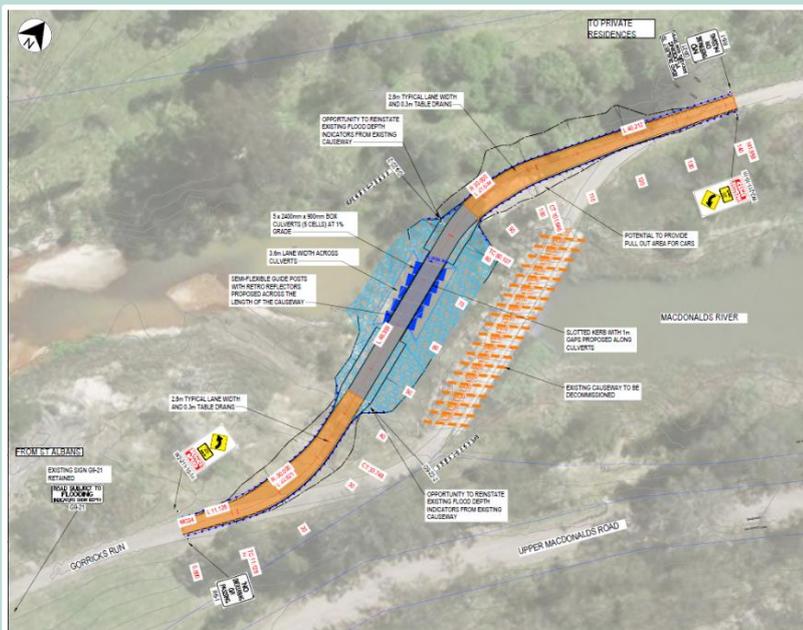

Turnbull Engineering have issued 80% design that has been reviewed by Council. HCC anticipate 100% design by 25 August 2023

A new box culvert crossing will be designed and constructed adjacent to existing, allowing for uninterrupted traffic flow for the community during the construction phase.

5T load limit signs have now been installed to replace the costly VMS boards currently onsite.

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

Major Landslips – Bowen Mountain Road, Bowen Mountain

Project Manager Rajesh Lama

Earthtec commenced embankment stabilisation work on Bowen Mountain Road 03 July 2023

Soil nailing has now been completed and shotcrete works commenced on Friday 25 August 2023. Stabilisation work is expected to be completed on 31 August 2023.

Bowen Mountain Road is open to two lane traffic of an evening and weekends. Stop/go traffic lights are still in operation on weekdays.



Major Landslips – Hulbert Road, Upper Colo

Project Managers Sadat Rahman



Retaining wall construction is now complete at both sites 1 and 2. Guideposts have been installed and drainage work has commenced this week. Jute matting will be laid below the sandstone walls next week to prepare for landscaping.

Hulbert Road will have unrestricted access from next month when the HCC Campground re-opens on 01 September 2023

The majority of the work is taking place below the slip at ground level while resident access along Hulbert Road is not affected.

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

MAJOR LANDSLIPS – Design

Project Manager Rajesh Lama



Chaseling Road North

ERM, Enstruct and Complete Urban are progressing the following designs and anticipate completion by 31 October 2023:

1. Chaseling Road North x1
2. Colo Heights Road x1
3. Crab Tree Gully Road x1
4. Grono Farm Road x1
5. Grose Vale Road x1
6. Reedy Road x1
7. Settlers Road x6
8. St Albans Road x9
9. Tizzana Road x1
10. Upper Macdonald Road x10
11. Wollombi Road x5

MINOR LANDSLIPS – In Procurement

Project Manager Rajesh Lama

Tender for the following landslips closed 18 August 2023. HCC received four responses from the panel contractor. Evaluation process in underway.

1. Argents Road x 1
2. Beaumont Avenue x 1
3. Crab Tree Gully Road x 1
4. Greens Road x 2
5. Lower Colo Road x 5
6. Sackville Road x 1
7. Settlers Road x 11
8. St Albans Road x 7
9. Tennyson Road x 1
10. Upper Colo Road x 1
11. Upper Macdonald Road x 1
12. Wheelbarrow Ridge Road x 2
13. Wollombi Road x4



Lower Colo Road

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

CORNWALLIS ROAD, CORNWALLIS – Riverbank & Drain Reconstruction

Project Manager Miro Cujic

STATE FUNDING FOR CORNWALLIS RESTORATION SECURED

Infrastructure NSW has advised that it has secured the State Government portion of funding for flood repairs at Cornwallis, including the repair of the flood mitigation system and the replacement of the missing section of Cornwallis Road.

The initial damage at Cornwallis was caused during the March 2021 flood, with the failure of the flood mitigation system and severe erosion of the riverbank. Subsequent flooding in 2022 caused further erosion and the breaching of the riverbank, resulting in a small bay forming. A 180-metre section of Cornwallis Road was also lost.

In support of Hawkesbury City Council, the NSW Government (led by Infrastructure NSW, NSW Public Works and the EPA) prepared a feasibility assessment to consider various infrastructure options to rebuild Cornwallis Road. Consultants and specialists were engaged to assess the options against multiple considerations to meet the following key objectives:

- Restore Cornwallis Road, including drainage and associated infrastructure
- Restore flood water behaviour to prior conditions
- Ensure the integrity of the land and sustainability of any solution
- Maintain the integrity of Bakers Lagoon, which is home to a number of endangered species

Following this detailed process, the option that has been identified by Infrastructure NSW is to restore Cornwallis Road on a 13-metre-high embankment and provide suitable drainage infrastructure under the road from Bakers Lagoon to the new bay. This option reinstates the natural levee function and the protection it provided to landowners. It will not restore the riverbank to its original alignment; the small bay will remain. The state funding means that discussions can commence with landowners regarding access and acquisitions while negotiations continue with the Federal Government for its contribution. It is anticipated the restoration works will take 12 months to complete pending finalisation of discussions with landowners. HCC will continue to hold the NSW Government to account on its commitment to timing and for the rapid approval of funding so we can get on with the job of repairing the damaged drain and reinstating the protection of the Cornwallis and Richmond Lowlands.



RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

WEBBS CREEK ROAD, Webbs Creek

Project Manager Shashi Mallegowda

Procurement for the restoration of Webbs Creek Road is currently taking place.

We anticipate commencement on site later this year.



GRAVEL ROADS – Crown roads

Project Manager Shashi Mallegowda



Perry Road/Perry's Run

The team visited four Crown Roads this week to confirm the extent of flood damage.

- Eternity Trail, Wheeny Creek
- Kaldow Lane, Grose Vale
- Mahons Creek Road, Yarramundi
- Perry Road, Perrys Crossing

Scope and estimating are currently in progress, once completed IRT will apply for DRFA funding from TfNSW.

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

GRAVEL ROADS – Pending Funding Approval

Avondale Road	Hall Street	Perry Road/Perry's Run (Crown)
Bicentenary Road	Hebron Road	Post Office Road
Brewers Lane	Hendrens Road	Punt Road
Brickfield Road	Irwins Road	Reedy Road
Browns Road	Jones Road	Sams Way
Burralow Road	Kaldow Lane (Crown)	Serpentine Lane
Chaseling Road South	Kandeer Road	Settlers Road
Colo Heights Road	Kolora Road	Stannix Park Lane
Comleroy Road	Laws Farm Road	Tennyson Road
Dickson Lane	Lower Colo Road	Triangle Lane
Doyles Creek Road	Mahons Creek Road (Crown)	Upper Colo Road
Eternity Trail (Crown)	Mckinnons Road	Upper Macdonald Road
Fairey Road	Mountain Lagoon Road	Webbs Creek Mountain Road
Geakes Road	Mullens Road	Webbs Creek Road
Greens Road	Nutmans Road	Wheelbarrow Ridge Road
Grose River Road	Old East Kurrajong Road	Wollombi Road
Gunbower Road	Paul Street	Wrights Creek Road
		Yarramundi Lane



RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

SEALED ROADS – In Procurement

Project Manager Shashi Mallegowda



Hibberts Lane

Tender for construction closed 18 July 2023 and contracts are being awarded to the successful contractors.

1. Cornwallis Road, Cornwallis
2. Cornwells Lane, Richmond Lowlands
3. Hibbert's Lane, Freemans Reach
4. Onus Lane, Richmond Lowlands
5. Pitt Town Ferry Road, Wilberforce
6. Saunders Road, Oakville

SEALED ROADS – In Planning

Project Manager Shashi Mallegowda

Durkin Construction commenced pavement investigations on Monday 21 August 2023.

1. Berger Road, South Windsor
2. Nutmans Road, Grose Wold
3. Spinks Road, Glossodia
4. Pitt Town Dural Road, Pitt Town
5. Pamela Crescent, Bowen Mountain
6. Schofield Road, Pitt Town
7. Stannix Park Road, Wilberforce
8. Walmsley Road, Lower Macdonald
9. Greenfield Place, Maraylya



Pitt Town Dural Road

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

SEALED ROADS PACKAGE – TfNSW Funding Approved

Andrew Thompson Drive	Grose River Road	Sackville Road
Argents Road	Hession Road	Ski Lodge Road
Argyle Reach Road	Industry Road	Slopes Road
Ashtons Road	Irwins Road	Smith Road
Bandon Road	King Road	Stannix Park Lane
Blackman Crescent	Manns Road	Stones Road
Blacktown Road	Max Street	Terrace Road
Bowen Mountain Road	McGrath Road	Tennyson Road
Buckingham Street	Mileham Street	The Driftway
Castlereagh Road	Morilla Road	The Terrace
Chaseling Road North	Mulgrave Road	Tizzana Road
Chisholm Place	North Street	Turnbull Avenue
Collith Avenue	Old East Kurrajong Road	Upper Colo Road
Commercial Road	Old Kurrajong Road	Uworra Road
Cordners Lane	Old Pitt Town Road	Valley Way
Coromandel Road	Old Sackville Road	Webbs Creek Road
Court Street	Palmer Street	West Portland Road
Crossley Avenue	Penruddock Street	Whitmore Road
Crowleys Lane	Pitt Town Bottoms Road	Wolseley Road
Curtis Road	Racecourse Road	Woods Road
Drummond Street	Railway Road South	Wheelbarrow Ridge Road
Dungullin Way	Reedy Road	Willeroo Drive
East Kurrajong Road	Rickaby Street	Wimbow Place
Edwards Road	Ridges Lane	Windsor Street
Fairey Road	Rifle Range Road	Wymarks Lane
Fisher Road	Riverside Drive	Yarramundi Lane
Gorricks Lane	Roberts Creek Road	
Greenway Crescent	Ross Street	
Grono Farm Road		

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

MISCELLANEOUS WORKS – Pending Funding Approval

Airstrip Road – Sealed pavement repairs
Ashtons Road – Table drain damage
Bandon Road – Table drain damage
Berger Road – Culvert/Floodway repairs
Bowen Mountain Rd – Sealed pavement repairs
Bradley Road – Cycleway damaged
Buckingham Street – Sealed pavement repairs
Bulga Street – Sealed pavement repairs
Burdekin Road – Stormwater
Castlereagh Road – Sealed pavement repairs
Commercial Road – Sealed pavement repairs
Duke Road – Sealed pavement repairs
Edwards Road – Sealed pavement repairs
Evans Road – Excessive material for removal
Freemans Reach Road – Table drain damage
Freemans Reach Road – Stormwater
Geakes Road – Sealed pavement repairs
Greenway Crescent – Table drain damage
Grono Farm Road – Guardrail damaged
Hadden Ridge Road – Sealed pavement repairs
Irwins Road – Table drain damage
Kentucky Drive – Table drain damage
Level Crossing Road – Stormwater
Madeleine Place – Sealed pavement repairs
Morilla Road – Sealed pavement repairs


Old Bells Line of Road – Bridge/Footbridge repairs
Old East Kurrajong Road – Table drain damage
Old Stock Route Road – Sealed pavement repairs
Reedy Road – Sealed pavement repairs
Reedy Road – Culvert/Floodway repairs
Roberts Creek Roads – Sealed pavement repairs
Scheyville Road – Table drain damage
Settlers Road – Culvert/Floodway repairs
Shepherds Road – Culvert/Floodway repairs
St Albans Road – Excessive material for removal
St Albans Road – Stormwater
St Albans Road – Table drain damage
Swallow Reach Place – Sealed pavement repairs
Tennyson Road – Table drain damage
Threlkeld Drive – Sealed pavement repairs
Tizzana Road – Stormwater
Tizzana Road – Bridge/Footbridge repairs
Upper Colo Road – Table drain damage
Upper Colo Road – Bridge handrail damage
Uworra Road – Sealed pavement repairs
West Portland Road – Stormwater

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

COMPLETED PROJECTS – Infrastructure Recovery

Upper Colo Road – Minor Landslips x 6	- Completed 02 November 2022
Pitt Town Dural Road – Sealed Roads	- Completed 19 October 2022
Settlers Road 1098 – Major Landslip	- Completed 21 September 2022
Upper Colo Road – Minor Landslips x 8	- Completed 07 September 2022
Old Stock Route Road – Sealed Roads	- Completed 23 August 2022
Inalls Lane – Sealed Roads	- Completed October 2022
Bowen Mountain Road – Major Landslip	- Completed 15 November 2022
King Road – Sealed Roads	- Completed 19 December 2022
Sackville Road – Sealed Roads	- Completed December 2022
West Portland Road – Sealed Roads	- Completed December 2022
Grono Farm Road – Sealed Roads	- Completed December 2022
Pitt Town Bottoms Rd – Sealed Roads	- Completed December 2022
Percival Street – Sealed Roads	- Completed 11 January 2023
Cupitts Lane – Sealed Roads	- Completed 5 April 2023
Brabyn Street – Sealed Roads	- Completed 8 May 2023
Upper Colo Road – Major Landslips x 2	- Completed 15 May 2023
Greens Road Site 1 and Site 2 – Major Projects	- Completed 16 June 2023
Upper Colo Bridge – Major Projects	- Completed 28 June 2023
Bensons Lane – Sealed Roads	- Completed 01 August 2023
Greens Road – Major Landslips x2	- Completed 11 August 2023

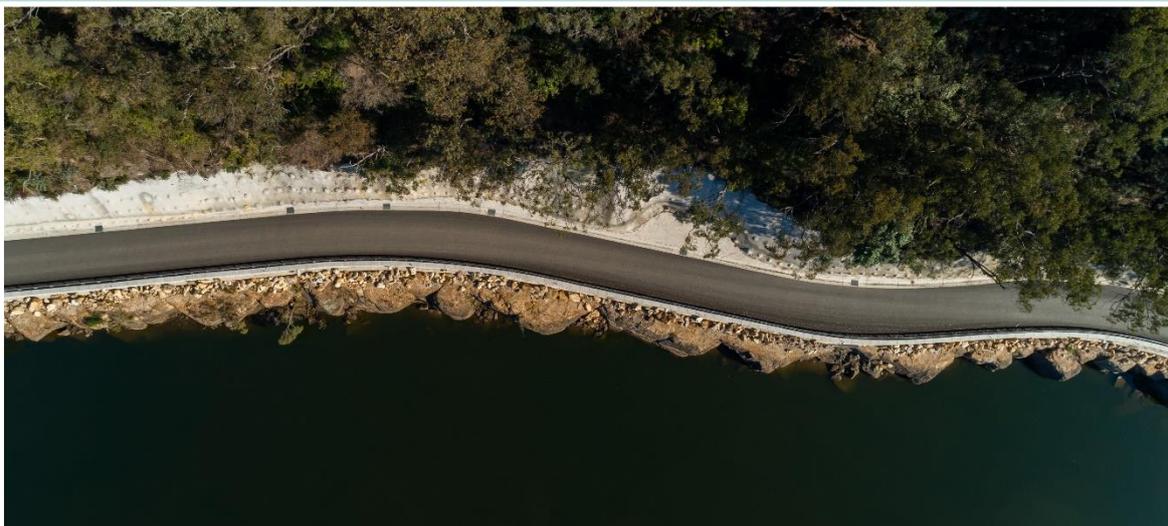

Greens Road, Lower Portland

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

OLD STOCK ROUTE ROAD, Oakville

Project Manager Hayden Jones



Road Rehabilitation has commenced on Old Stock Route Road, Oakville.

The section between Saunders and Scheyville Road will see 220m of pavement improvements. This works is part of a TfNSW funded project.

Line marking and guidepost installation continues this week.

Traffic control are on site to maintain safe thoroughfare.

ST ALBANS ROAD, Lower Macdonald

Project Manager Dhruba Bhowmik



Road reconstruction and drainage improvements have commenced to a 500m section of St Albans Road.

Clearing road edges and drainage works continue this week.

Traffic control is in operation on site ensuring safety of motorists.

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

MITCHELL DRIVE, Glossodia

Project Manager Dhruba Bhowmik

Road widening, new kerb and gutter and underground drainage is 90% complete.

Landscaping has commenced this week and final wearing course will also be laid.

Please follow site directions and speed limits as detours are in place.



IAN STREET, Glossodia

Project Manager Dhruba Bhowmik



Road widening and underground drainage is complete.

Kerb and gutter are being installed over the coming weeks.

Residents are asked to follow contractor's instructions to manoeuvre safely through site.

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

RLRRP – Scheduled Works

Project Manager Steve Burns

Spinks Road (Package 1) – Work commenced 15 August 2023
 Cabbage Tree Road (Package 2) – Work commenced 21 August 2023
 Grose Vale Road (Package 2) – Work commenced 22 August 2023
 Old Bells Line Road – Scheduled to commence 28 August 2023



Grose Vale Road

COMPLETED PROJECTS – RLRRP

Project Manager Steve Burns

Tizzana Road (Package 1)	- Completed 30 May 2023
Sackville Road (Package 1)	- Completed 01 June 2023
Golden Valley Drive (Package 1)	- Completed 09 June 2023
Southee Road (Priority Repair)	- Completed 14 July 2023
Blaxlands Ridge Road (Package 2)	- Completed 21 July 2023
East Kurrajong Road (Package 2)	- Completed 27 July 2023
Comleroy Road (Package 2)	- Completed 31 July 2023
Bull Ridge Road (Package 2)	- Completed 31 July 2023
Kurmond Road (Package 2)	- Completed 03 August 2023
St Albans Road (Package 1)	- Completed 04 August 2023
Tasman Place (Package 2)	- Completed 09 August 2023
Slopes Road (Package 1)	- Completed 14 August 2023
Terrace Road (Package 1)	- Completed 19 August 2023

RENEWING HAWKESBURY'S ROADS

Weekly Roads Update

OLD PITT TOWN ROAD, PITT TOWN – Flood Evacuation Route

Project Manager Steve Burns

Six sections of Old Pitt Town Road are being completed by our Transport Operations Team. Sites 1, 2, 4 and 6 are complete.

Work on Site 3 re-commenced Monday 21 August 2023. Once completed 9500m² of Road Pavement will have been repaired.

Site 3 is located on Old Pitt Town Road between Scheyville Road and the National Park entrance.

